

STORMWATER MANAGEMENT PLAN & DRAINAGE ANALYSIS

**54 Clinton Avenue
Village of Dobbs Ferry – New York**

November 18, 2021



Hudson Engineering & Consulting, P.C.

45 Knollwood Road – Suite 201

Elmsford, NY 10523

(914) 909-0420

**STORMWATER MANAGEMENT
PLAN & DRAINAGE ANALYSIS
54 Clinton Avenue
Village of Dobbs Ferry – New York**

INTRODUCTION

This Stormwater Management Plan presents the proposed Best Management Practices (BMPs) to control erosion and sedimentation and manage stormwater during and upon construction of proposed pool and patio at 54 Clinton Avenue in the Village of Dobbs Ferry, Westchester County, New York.

This Plan consists of this narrative and a plan set entitled: “Proposed Additions & Alterations, 54 Clinton Avenue, Village of Dobbs Ferry, Westchester County - New York”, all as prepared by Hudson Engineering and Consulting, P.C., Elmsford, New York, last dated November 18, 2021. The design is in accordance with the Village of Dobbs Ferry requirements. Since the project disturbance is less than one acre the New York State Department of Environmental Conservation [NYSDEC] stormwater regulations are not applicable.

METHODOLOGY

The stormwater analysis was developed utilizing the Soil Conservation Service (SCS) TR-20, 24-hour Type III storm events (HydroCad®) to assist with the design of the mitigating practices. The “Curve Number” (CN) value determination is based on soil type, vegetation and land use. The design is in accordance with the Village of Dobbs Ferry stormwater regulations. The “Time of Concentration” (T_c) was determined as a direct entry of one-minute. The CN and T_c data are input into the computer model. The project site was modeled for the 100-year Type III – 24-hour storm event.

PRE-DESIGN INVESTIGATIVE ANALYSIS

A pre-design investigative analysis was performed including percolation and deep tests in the location shown on the plans.

Percolation tests were completed as follows: A 36-inch deep hole was excavated and an 8-inch percolation test hole was excavated approximately 24 inches in the hole. A 4-inch diameter pipe was inserted into the percolation hole and backfilled around. The hole was pre-soaked for 24 hours prior to running the tests. The pipe was filled with 24 inches of water and monitored for 1 hour or until the test-hole completely drained, whichever came first. The runs were repeated for a minimum of 4 runs and a consistent percolation rate. Percolation tests were performed in the vicinity of the potential stormwater mitigation practice [TP-1] until a constant rate was achieved, the result as follows:

- TP-1: A percolation rate of 0.375-minutes per inch (160-inches per hour) was observed. A rate of 30-inches per hour was utilized in the design.

A deep-hole test was also excavated and labeled TP-1 as shown on the plans.

- TP-1 was excavated to a depth of 98-inches. The test revealed topsoil to a depth of 6-inches, fine brown sandy loam to a depth of 36-inches and mixed sands with small rocks to the invert. Neither ledge rock nor groundwater was encountered.

The deep-hole test log and percolation test data sheets are attached.

PRE-DEVELOPED CONDITION

In the pre-developed condition, the site is characterized as sloping from the southeast to northwest. The soil classification, based upon Westchester County Soils Mapping is Paxton fine sandy loam, 3 to 8 percent slopes. The site vegetation can be characterized as lawn and landscaped. The site is located along the west side of Clinton Avenue. Runoff from the existing site flows overland to the northwest corner of the property and existing the site.

POST-DEVELOPED CONDITION

The project site was modeled as one watershed, Watershed 1, which contains a tributary area of approximately 5,825 square feet, all of which are impervious in the form of proposed addition, garage and driveway. The CN value for this area is 98 and the Time of Concentration (Tc) is a direct entry of 1 minute. The runoff from this tributary area is conveyed via a comprehensive drainage system to ten (10) Cultec® Recharger 330XLHD units set in one foot of gravel at the sides and invert. The system is designed to fully accept (no release) the entire stormwater runoff volume for the 100-year storm event from the watershed and ex-filtrate the runoff into the surrounding soil sub-strata.

EROSION AND SEDIMENT CONTROL COMPONENTS

The primary aim of the soil and sediment control measures is to reduce soil erosion from areas stripped of vegetation during and after construction and to prevent silt from reaching the off-site drainage structures and downstream properties. The Sediment and Erosion Control Components are an integral component of the construction sequencing and will be implemented to control sedimentation and re-establish vegetation.

Planned erosion and sedimentation control practices during construction include the installation, inspection and maintenance of the inlet protection, soil stockpile areas, and diversion swales and silt fencing. General land grading practices, including land stabilization and construction sequencing are also integrated into the Sediment and Erosion Control Plan. Dust control is not expected to be a problem due to the relatively limited area of exposure, the undisturbed perimeter

of trees around the project area and the relatively short time of exposure. Should excessive dust be generated, it will be controlled by sprinkling.

All proposed soil erosion and sediment control practices have been designed in accordance with the following publications:

- New York State standards and Specifications for Erosion and Sediment Control, November 2016
- New York State General Permit for Stormwater Discharges, GP-0-20-001 (General permit).
- "Reducing the Impacts of Stormwater Runoff from New Development", as published by the New York State Department of Environmental Conservation (NYSDEC), second edition, April, 1993.

The proposed soil erosion and sediment control devices include the planned erosion control practices outlined below. Maintenance procedures for each erosion control practice have also been outlined below.

• **SILT FENCE**

Silt fence (geo-textile filter cloth) shall be placed in locations depicted on the approved plans. The purpose of the silt fence is to reduce the velocity of sediment laden stormwater from small drainage areas and to intercept the transported sediment load. In general, silt fence shall be used at the toe of slopes or intermediately within slopes where obvious channel concentration of stormwater is not present.

Maintenance

Silt fencing shall be inspected at a minimum of once per week and prior to and within 24 hours following a rain event $\frac{1}{2}$ " or greater. Inspections shall include ensuring that the fence material is tightly secured to the woven wire and the wire is secured to the wood posts. In addition, overlapping filter fabric shall be secured and the fabric shall be maintained a minimum of six (6) inches below grade. In the event that any "bulges" develop in the fence, that section of fence shall be replaced within 24 hours with new fence section. Any sediment build-up against the fence shall be removed within 24 hours and deposited on-site a minimum of 100 feet outside of any wetland or watercourse.

The installation of silt fencing will be maintained or replaced until the fencing is no longer necessary. Once the site is stabilized, all silt fences shall be removed. The immediate area occupied by the silt fence will be shaped to an acceptable grade and stabilized.

- **INLET PROTECTION**

After catch basins and surface inlets have been installed, these drain inlets will receive stormwater from the roadways, driveways, and surrounding overland watersheds. In order to protect the receiving waters from sedimentation, the contractor shall install stone and block inlet protection as shown on the plans. Once installed, $\frac{3}{4}$ inch stone aggregate shall be installed around the perimeter of all catch basins and surface inlets as illustrated on the approved plans. This barrier will allow stormwater to be filtered prior to reaching the basin inlet grate.

The stone barrier should have a minimum height of 1 foot and a maximum height of 2 feet. Do not use mortar. The height should be limited to prevent excess ponding and bypass flow. Recess the first course of blocks at least 2 inches below the crest opening of the storm drain for lateral support. Subsequent courses can be supported laterally if needed by placing a 2x4 inch wood stud through the block openings perpendicular to the course. The bottom row should have a few blocks oriented so flow can drain through the block to dewater the basin area. The stone should be placed just below the top of the blocks on slopes of 2:1 or flatter. Place hardware cloth or wire mesh with $\frac{1}{2}$ inch openings over all block openings to hold stone in place.

As an optional design, the concrete blocks may be omitted and the entire structure constructed of stone, ringing the outlet ("doughnut"). The stone should be kept at a 3:1 slope toward the inlet to keep it from being washed into the inlet.

A level area 1 foot wide and four inches below the crest will further prevent wash. Stone on the slope toward the inlet should be at least 3 inches in size for stability and 1 inch or smaller away from the inlet to control flow rate. The elevation of the top of the stone crest must be maintained 6 inches lower than the ground elevation down slope from the inlet to ensure that all storm flows pass over the stone into the storm drain and not past the structure.

The barrier should be inspected after each rain event and repairs made within 24 hours. Remove sediment as necessary to provide for accurate storage volume for subsequent rains. Upon stabilization of contributing drainage area, remove all materials and any unstable soil and dispose of properly. Bring the disturbed area to proper grade, smooth, compact and stabilized in a manner appropriate to the site.

Maintenance

Stone Aggregate: The stone aggregate shall be inspected weekly prior to and within 24 hours following a rain event $\frac{1}{2}$ " or greater. Care shall be taken to ensure that all stone aggregate is properly located and secure and do not become displaced. The stone aggregate shall be inspected for accumulated

sediments and any accumulated sediment shall be removed from the device and deposited not less than 100 feet from wetland or watercourse.

- **TREE PROTECTION**

All significant trees to be preserved located within the limits of disturbance and on the perimeter of the disturbance limits shall be protected from harm by erecting a 3' high (minimum) snow fence completely surrounding the tree. Snow fence should extend to the drip-line of the tree to be preserved. Trees designated to be protected shall be identified during the staking of the limits of disturbance for each construction phase.

Maintenance

The snow fence shall be inspected daily to ensure that the perimeter of the fence remains at the drip-line of the tree to be preserved. Any damaged portions of the fence shall be repaired or replaced within 24 hours. Care shall also be taken to ensure that no construction equipment is driven or parked within the drip-line of the tree to be preserved.

- **SOIL/SHOT ROCK STOCKPILING**

All soil and shot rock stripped from the construction area during grubbing and mass grading shall be stockpiled in locations shown on the plans, but in no case shall they be placed within 100' of a wetland or watercourse. The stockpiled soils shall be re-used during finish-grading to provide a suitable growing medium for plant establishment. Soil stockpiles shall be protected from erosion by vegetating the stockpile with rapidly –germinating grass seed (during the May 1st – October 30th) planting season or covering the stockpile with tarpaulin the remainder of the year. Install silt fence around toe of slope.

Maintenance

Sediment controls (silt fence) surrounding the stockpiles shall be inspected according to the recommended maintenance outline above. *All stockpiles shall be inspected for signs of erosion or problems with seed establishment weekly or tarpaulin and prior to and within 24 hours following a rain event ½" or greater.*

- **GENERAL LAND GRADING**

The intent of the Erosion & Sediment Control Plan is to control disturbed areas such that soils are protected from erosion by temporary methods and, ultimately, by permanent vegetation. Where practicable, all cut and fill slopes shall be kept to a maximum slope of 2:1. In the event that a slope must exceed a 2:1 slope, it will be stabilized with stone riprap. On fill slopes, all material will be placed in layers not to exceed 12 inches in depth and

adequately compacted. Diversion swales shall be constructed on the top of all fill embankments to divert any overland flows away from the fill slopes.

- **SURFACE STABILIZATION**

All disturbed areas will be protected from erosion with the use of vegetative measures (i.e., grass seed mix, sod) hydro mulch netting or hay. When activities temporarily cease during construction, soil stockpiles and exposed soil should be stabilized by seed, mulch or other appropriate measures within 7 days after construction activity has ceased, or 24 hours prior to a rain event $\frac{1}{2}$ " or greater.

All seeded areas will be re-seeded areas as necessary and mulched according to the site plan to maintain a vigorous, dense vegetative cover,

Erosion control barriers (silt fencing) shall be placed around exposed areas during construction. Where exposed areas are immediately uphill from a wetland or watercourse, the erosion control barrier will consist of double rows of silt fencing. Any areas stripped of vegetation during construction will be vegetated and/or mulch, but in no case more than 14 days to prevent erosion of the exposed soils. And topsoil removed during construction will be temporarily stockpiled for future use in grading and landscaping.

As mentioned above, temporary vegetation will be established to protect exposed soil areas during construction. If growing conditions are not suitable for the temporary vegetation, mulch will be used to the satisfaction of the Town Engineer. Materials that may be used for mulching include straw, hay, salt hay, wood fiber, synthetic soil stabilizers, mulch netting, sod or hydro mulch. In site areas where significant erosion potential exists (steep slopes) and where specifically directed by the Town's representative, Curlex Excelsior erosion control blankets (manufactured by American Excelsior, or approved equal) shall be installed. A permanent vegetative cover will be established upon completion of construction of those areas that have been brought to finish-grade and to remain undisturbed.

- **Temporary Stabilization(May 1st through October 31st planting season)**

The following seeding application should be used depending on the time of year.

- Spring/summer or early fall, seed the area with ryegrass (annual or perennial) at 30 lbs. per acre (Approximately 0.7 lb/1000 sq. ft. or use 1 lb/1000 sq. ft.).
- Late fall or early winter, seed Certified 'Aroostook' winter rye (cereal rye) at 100 lbs. per acre (2.5 lbs/1000 sq. ft.).

- **Permanent Stabilization(May 1st through October 31st planting season)**

1. Provide minimum of four (4) inches topsoil for all new lawn areas. Top dress all existing disturbed lawn areas with two (2) inches of topsoil.
2. Grass seed shall be evenly sown by mechanical seeder at a rate of 3.0-4.0 pounds per 1,000 square feet.
3. Fine rake, roll and water to a depth of one inch all seeded areas.
4. Apply air-dried hay or straw mulch to provide 90% coverage of surface (approximately 90 lbs. per 1,000 SF). Use small grain straw where mulch is maintained for more than three months
5. Contractor shall provide, at his own expense, protection against trespassing and other damage to lawn areas.
6. Lawn seed mix shall include:
 - a. General Recreation areas and lawns:
 - 65% Kentucky Bluegrass blend
 - 20% Perennial Rye
 - 15% Fine fescue

Sod may be used as an alternate to seeding in select areas.

Slow release fertilizers will be applied by hand to horticultural plantings as part of regular horticultural maintenance program and shall be limited to a single spring application.

CONSTRUCTION PRACTICES TO MINIMIZE STORMWATER CONTAMINATION

Adequate measures shall be taken to minimize contaminant particles arising from the discharge of solid materials, including building materials, grading operations, and the reclamation and placement of pavement, during project construction, including but not limited to:

- Building materials, garbage, and debris shall be cleaned up daily and deposited into dumpsters, which will be periodically removed from the site and appropriately disposed of.
- Dump trucks hauling material from the construction site will be covered with a tarpaulin.
- The paved street adjacent to the site entrance will be swept daily to remove excess mud, dirt, or rock tracked from the site.

- Petroleum products will be stored in tightly sealed containers that are clearly labeled.
- All vehicles on site will be monitored for leaks and receive regular preventive maintenance to reduce the chance of leakage.
- All spills will be cleaned up immediately upon discovery. Spills large enough to reach the storm system will be reported to the National Response Center at 1-800-424-8802.
- Materials and equipment necessary for spill cleanup will be kept in the temporary material storage trailer onsite. Equipment will include, but not be limited to, brooms, dust pans, mops, rags, gloves, goggles, kitty litter, sand, saw dust, and plastic and metal trash containers.
- All paint containers and curing compounds will be tightly sealed and stored when not required for use. Excess paint will not be discharged to the storm system, but will be properly disposed according to the manufacturer's instructions.
- Sanitary waste will be collected from portable units a minimum of two times a week to avoid overfilling.
- Any asphalt substances used on-site will be applied according to the manufacturer's recommendation.
- Fertilizers will be stored in a covered shed and partially used bags will be transferred to a sealable bin to avoid spills and will be applied only in the minimum amounts recommended by the manufacturer and worked into the soil to limit exposure to stormwater.
- No disturbed area shall be left un-stabilized for longer than 14 days during the growing season.
- When erosion is likely to be a problem, grubbing operations shall be scheduled and performed such that grading operations and permanent erosion control features can follow within 24 hours thereafter.
- As work progresses, patch seeding shall be done as required on areas previously treated to maintain or establish protective cover.
- Drainage pipes and swales/ditches shall generally be constructed in a sequence from outlet to inlet in order to stabilize outlet areas and ditches before water is directed to the new installation or any portion thereof, unless conditions unique to the location warrant an alternative method.

STORMWATER MANAGEMENT FACILITIES MAINTENANCE PROGRAM

The following maintenance plan has been developed to maintain the proper function of all drainage and erosion and sediment control facilities:

- Minimize the use of road salt for maintenance of driveway areas.
- Drainage inlets shall be vacuum swept twice a year, at the conclusion of the landscape season in the fall and at the conclusion of the sand and de-icing season in the spring. Inspect exfiltration/attenuation gallery for sediment and remove same if found.


The permanent maintenance program will be managed by the future homeowners upon completion of construction and acceptance of the improvements.

CONCLUSION

The stormwater management plan proposed meets all the requirements set forth by the Village of Dobbs ferry. Design modification requirements that may occur during the approval process will be performed and submitted for review to the Village of Dobbs Ferry.

Soils Maps & Soils Data

Hydrologic Soil Group—Westchester County, New York

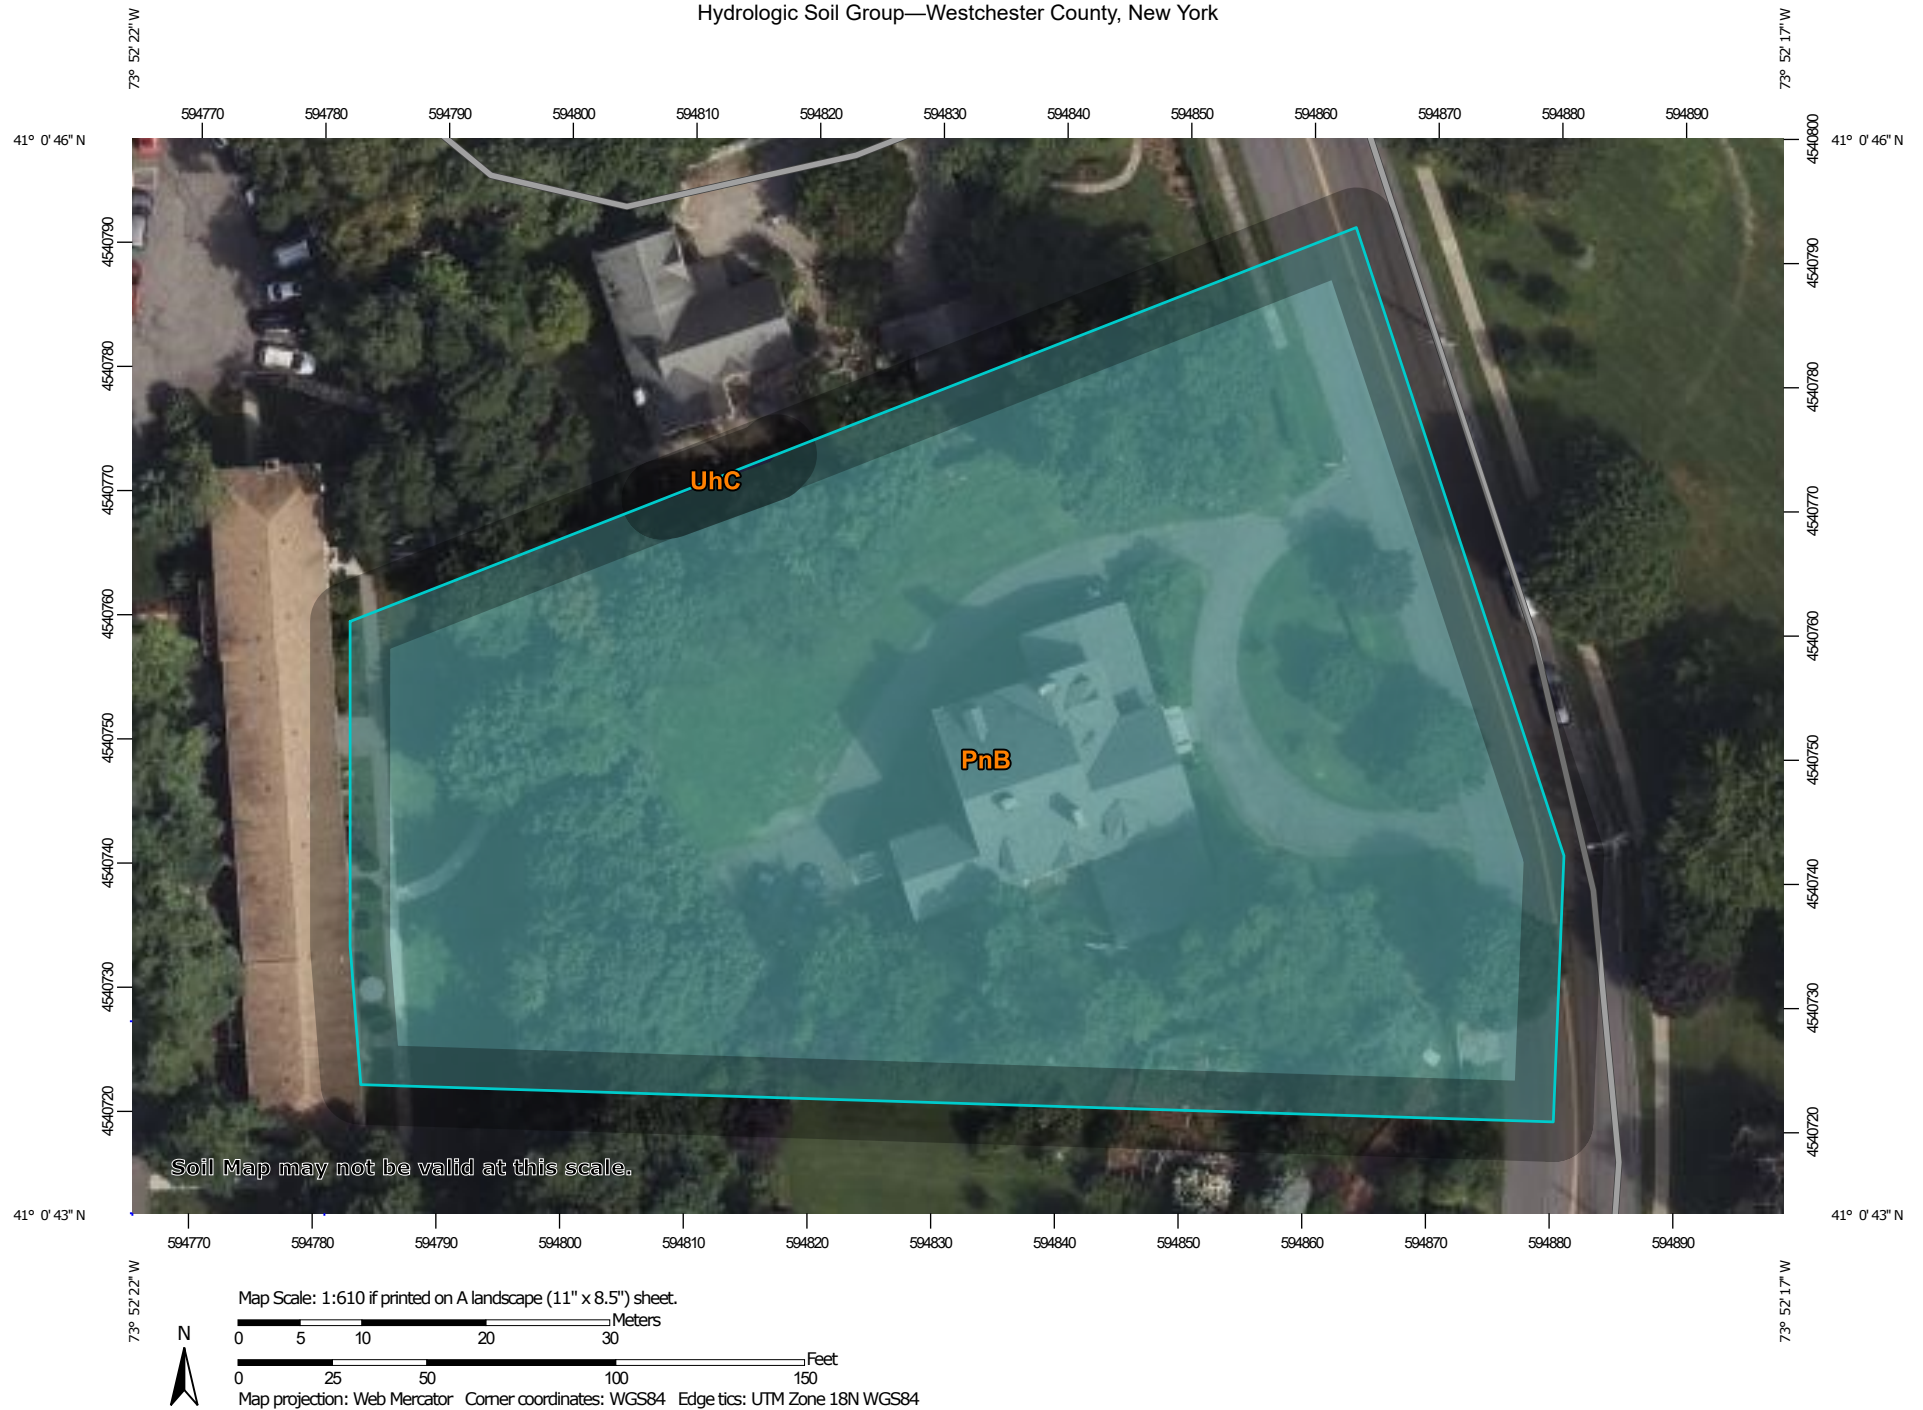

**Natural Resources
Conservation Service**

Web Soil Survey
National Cooperative Soil Survey

11/16/2021
Page 1 of 4

MAP LEGEND

Area of Interest (AOI)









 Area of Interest (AOI)

Soils

Soil Rating Polygons





 A
 A/D
 B
 B/D
 C
 C/D
 D
 Not rated or not available

Soil Rating Lines


 A
 A/D
 B
 B/D
 C
 C/D
 D
 Not rated or not available

Soil Rating Points






 A
 A/D
 B
 B/D

 C
 C/D
 D
 Not rated or not available


Water Features

 Streams and Canals

Transportation

 Rails
 Interstate Highways
 US Routes
 Major Roads
 Local Roads

Background

 Aerial Photography

MAP INFORMATION

The soil surveys that comprise your AOI were mapped at 1:12,000.

Warning: Soil Map may not be valid at this scale.

Enlargement of maps beyond the scale of mapping can cause misunderstanding of the detail of mapping and accuracy of soil line placement. The maps do not show the small areas of contrasting soils that could have been shown at a more detailed scale.

Please rely on the bar scale on each map sheet for map measurements.

Source of Map: Natural Resources Conservation Service
 Web Soil Survey URL:
 Coordinate System: Web Mercator (EPSG:3857)

Maps from the Web Soil Survey are based on the Web Mercator projection, which preserves direction and shape but distorts distance and area. A projection that preserves area, such as the Albers equal-area conic projection, should be used if more accurate calculations of distance or area are required.

This product is generated from the USDA-NRCS certified data as of the version date(s) listed below.

Soil Survey Area: Westchester County, New York
 Survey Area Data: Version 17, Sep 1, 2021

Soil map units are labeled (as space allows) for map scales 1:50,000 or larger.

Date(s) aerial images were photographed: Apr 13, 2021—Sep 14, 2021

The orthophoto or other base map on which the soil lines were compiled and digitized probably differs from the background imagery displayed on these maps. As a result, some minor shifting of map unit boundaries may be evident.

Hydrologic Soil Group

Map unit symbol	Map unit name	Rating	Acres in AOI	Percent of AOI
PnB	Paxton fine sandy loam, 3 to 8 percent slopes	C	1.3	100.0%
UhC	Urban land-Charlton complex, 8 to 15 percent slopes	B	0.0	0.0%
Totals for Area of Interest			1.3	100.0%

Description

Hydrologic soil groups are based on estimates of runoff potential. Soils are assigned to one of four groups according to the rate of water infiltration when the soils are not protected by vegetation, are thoroughly wet, and receive precipitation from long-duration storms.

The soils in the United States are assigned to four groups (A, B, C, and D) and three dual classes (A/D, B/D, and C/D). The groups are defined as follows:

Group A. Soils having a high infiltration rate (low runoff potential) when thoroughly wet. These consist mainly of deep, well drained to excessively drained sands or gravelly sands. These soils have a high rate of water transmission.

Group B. Soils having a moderate infiltration rate when thoroughly wet. These consist chiefly of moderately deep or deep, moderately well drained or well drained soils that have moderately fine texture to moderately coarse texture. These soils have a moderate rate of water transmission.

Group C. Soils having a slow infiltration rate when thoroughly wet. These consist chiefly of soils having a layer that impedes the downward movement of water or soils of moderately fine texture or fine texture. These soils have a slow rate of water transmission.

Group D. Soils having a very slow infiltration rate (high runoff potential) when thoroughly wet. These consist chiefly of clays that have a high shrink-swell potential, soils that have a high water table, soils that have a claypan or clay layer at or near the surface, and soils that are shallow over nearly impervious material. These soils have a very slow rate of water transmission.

If a soil is assigned to a dual hydrologic group (A/D, B/D, or C/D), the first letter is for drained areas and the second is for undrained areas. Only the soils that in their natural condition are in group D are assigned to dual classes.


Rating Options

Aggregation Method: Dominant Condition

Component Percent Cutoff: None Specified

Tie-break Rule: Higher

Watershed Maps

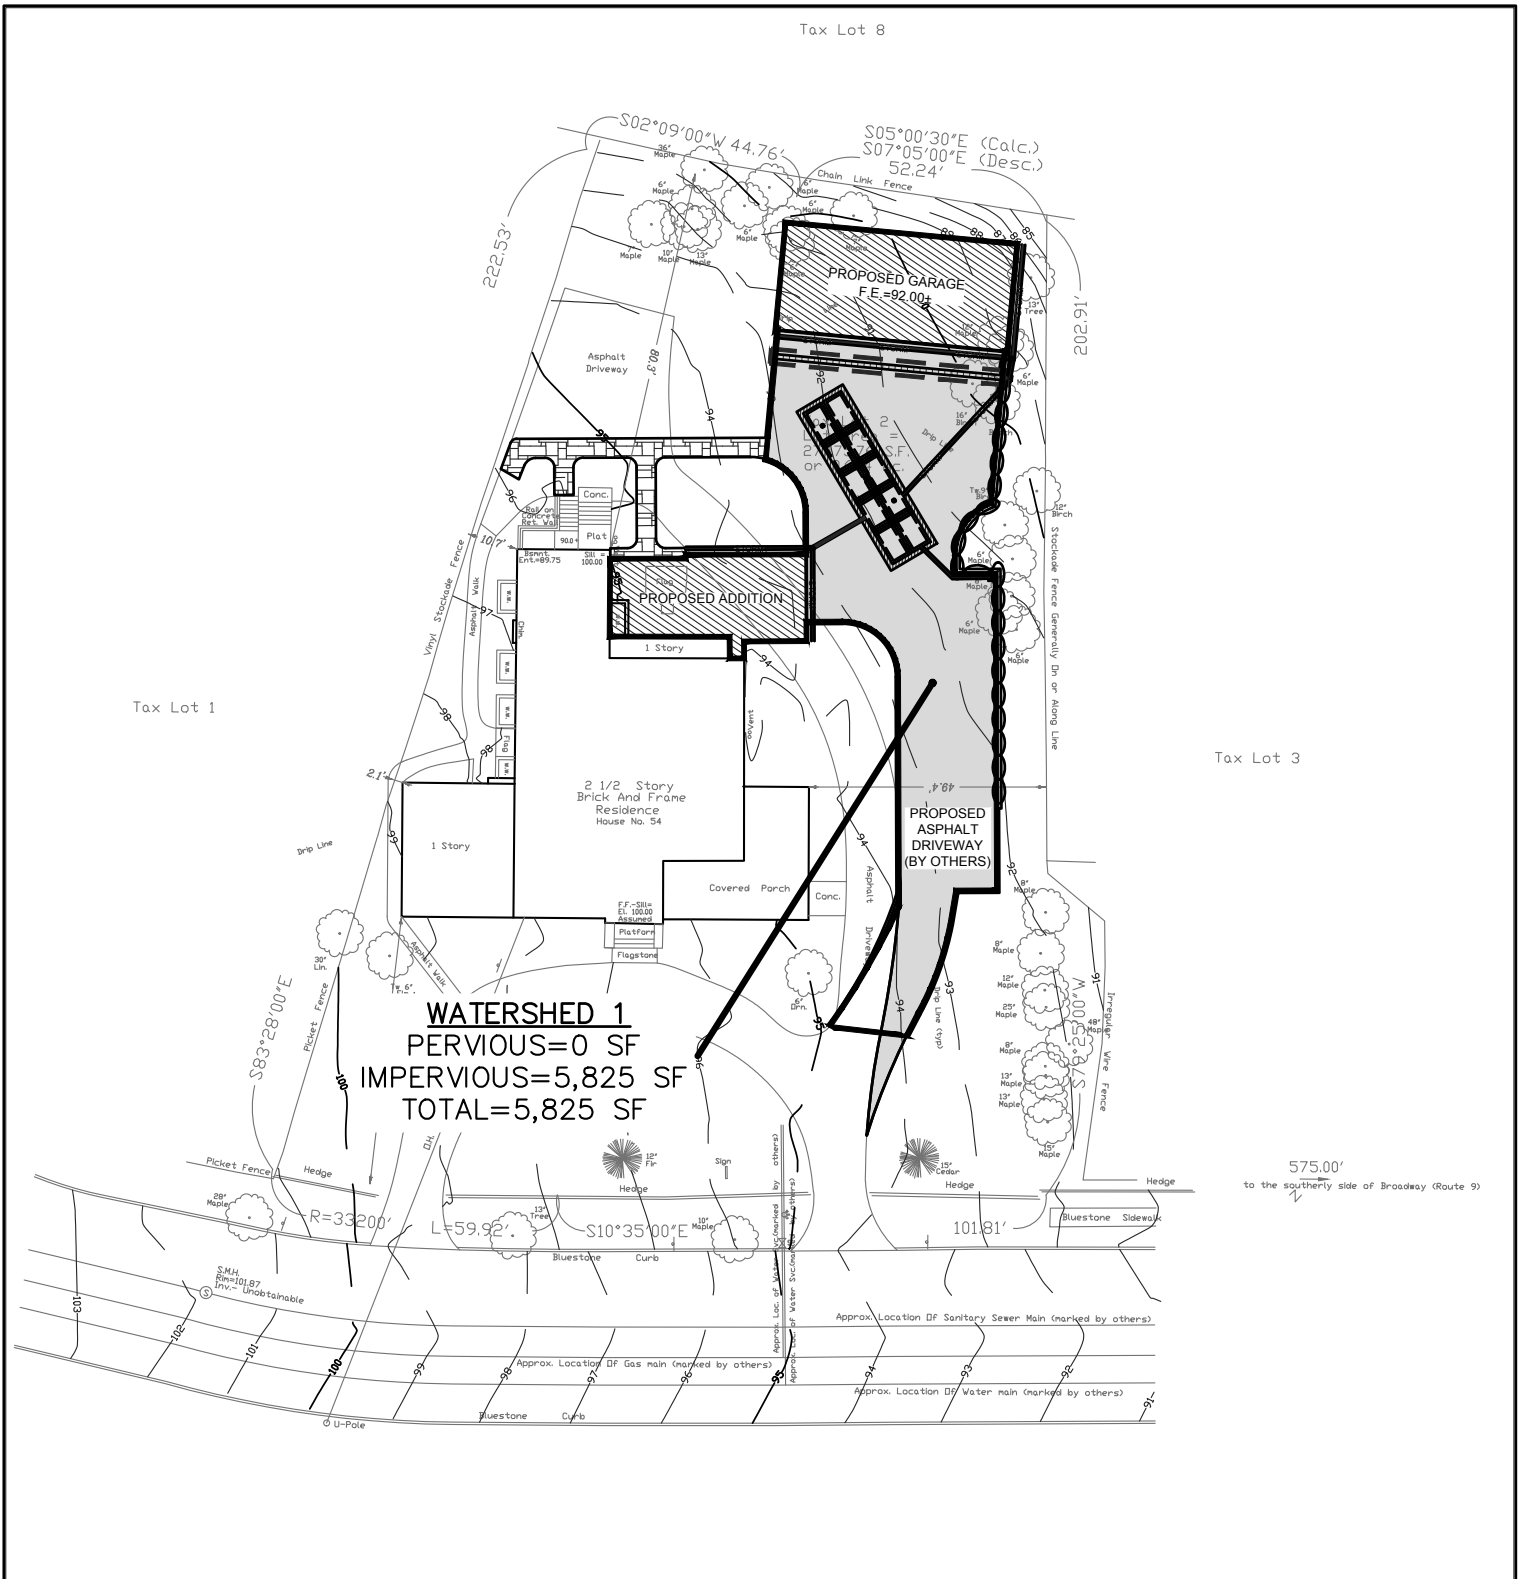

PROJECT: PROPOSED ADDITION & ALTERATIONS
 54 CLINTON AVENUE
 VILLAGE OF DOBBS FERRY
 WESTCHESTER COUNTY – NEW YORK

ANY ALTERATIONS OR REVISIONS OF THESE PLANS, UNLESS DONE BY OR UNDER THE DIRECTION OF THE NYS LICENSED AND REGISTERED ENGINEER THAT PREPARED THEM, IS A VIOLATION OF THE NYS EDUCATION LAW.

No.	Description	Date
Revisions		

THIS PLAN NOT VALID FOR CONSTRUCTION WITHOUT ENGINEERS SEAL & SIGNATURE

TITLE: WATERSHED MAP ANALYSIS PLAN = PROPOSED

HEC

HUDSON
ENGINEERING
 &
CONSULTING, P.C.
 45 Knollwood Road – Suite 201
 Elmsford, NY 10523

T: 914-909-0420
 F: 914-560-2086

Date: 11/18/21 Sheet: 1
 Scale: 1"=20'
 Drawn By: S.G.
 Checked By: M.S.
 Sheet No.

WS-P

© 2021

Extreme Percolation Tables

Extreme Precipitation Tables

Northeast Regional Climate Center

Data represents point estimates calculated from partial duration series. All precipitation amounts are displayed in inches.

Smoothing	Yes
State	New York
Location	
Longitude	73.872 degrees West
Latitude	41.012 degrees North
Elevation	0 feet
Date/Time	Tue, 16 Nov 2021 13:23:59 -0500

Extreme Precipitation Estimates

	5min	10min	15min	30min	60min	120min		1hr	2hr	3hr	6hr	12hr	24hr	48hr		1day	2day	4day	7day	10day	
1yr	0.33	0.51	0.63	0.82	1.03	1.29	1yr	0.89	1.23	1.48	1.84	2.27	2.81	3.20	1yr	2.49	3.08	3.57	4.29	4.93	1yr
2yr	0.40	0.62	0.77	1.01	1.27	1.59	2yr	1.10	1.49	1.83	2.26	2.78	3.42	3.85	2yr	3.03	3.70	4.26	5.05	5.73	2yr
5yr	0.47	0.73	0.91	1.23	1.57	1.98	5yr	1.35	1.84	2.29	2.84	3.49	4.28	4.87	5yr	3.78	4.68	5.43	6.33	7.08	5yr
10yr	0.53	0.83	1.04	1.42	1.84	2.34	10yr	1.59	2.17	2.72	3.37	4.14	5.06	5.82	10yr	4.48	5.59	6.53	7.50	8.32	10yr
25yr	0.61	0.97	1.24	1.71	2.28	2.93	25yr	1.97	2.69	3.41	4.24	5.22	6.34	7.37	25yr	5.61	7.09	8.33	9.40	10.29	25yr
50yr	0.69	1.11	1.43	2.00	2.68	3.48	50yr	2.32	3.17	4.06	5.05	6.19	7.51	8.82	50yr	6.65	8.48	10.03	11.15	12.10	50yr
100yr	0.78	1.27	1.64	2.32	3.16	4.13	100yr	2.73	3.74	4.82	6.01	7.36	8.91	10.55	100yr	7.89	10.15	12.07	13.23	14.23	100yr
200yr	0.89	1.45	1.88	2.70	3.73	4.90	200yr	3.22	4.41	5.73	7.15	8.76	10.58	12.63	200yr	9.36	12.15	14.54	15.70	16.74	200yr
500yr	1.07	1.75	2.29	3.32	4.65	6.14	500yr	4.01	5.50	7.21	9.00	11.02	13.28	16.04	500yr	11.75	15.42	18.61	19.70	20.76	500yr


Lower Confidence Limits

	5min	10min	15min	30min	60min	120min		1hr	2hr	3hr	6hr	12hr	24hr	48hr		1day	2day	4day	7day	10day	
1yr	0.30	0.46	0.56	0.75	0.92	1.13	1yr	0.80	1.11	1.31	1.55	2.17	2.44	2.62	1yr	2.16	2.52	3.29	3.99	4.37	1yr
2yr	0.38	0.59	0.73	0.98	1.21	1.46	2yr	1.05	1.43	1.67	2.17	2.69	3.32	3.73	2yr	2.94	3.59	4.12	4.88	5.55	2yr
5yr	0.41	0.64	0.79	1.08	1.38	1.70	5yr	1.19	1.67	1.96	2.51	3.16	3.97	4.51	5yr	3.51	4.34	4.99	5.82	6.52	5yr
10yr	0.44	0.68	0.84	1.18	1.52	1.89	10yr	1.31	1.85	2.19	2.75	3.56	4.55	5.20	10yr	4.03	5.00	5.73	6.62	7.28	10yr
25yr	0.48	0.73	0.90	1.29	1.69	2.17	25yr	1.46	2.12	2.54	3.09	4.17	5.47	6.26	25yr	4.85	6.02	6.85	7.89	8.32	25yr
50yr	0.50	0.76	0.95	1.36	1.83	2.40	50yr	1.58	2.34	2.84	3.35	4.69	6.30	7.21	50yr	5.58	6.93	7.79	8.98	9.12	50yr
100yr	0.52	0.79	0.99	1.43	1.96	2.63	100yr	1.69	2.57	3.16	3.60	5.25	7.27	8.29	100yr	6.43	7.97	8.90	10.23	9.94	100yr
200yr	0.54	0.81	1.02	1.48	2.07	2.87	200yr	1.78	2.81	3.53	3.84	5.91	8.41	9.52	200yr	7.44	9.16	10.14	11.65	10.77	200yr
500yr	0.55	0.83	1.06	1.54	2.19	3.23	500yr	1.89	3.15	4.08	4.13	6.93	10.21	11.37	500yr	9.03	10.93	12.01	13.81	11.88	500yr


Upper Confidence Limits

	5min	10min	15min	30min	60min	120min		1hr	2hr	3hr	6hr	12hr	24hr	48hr		1day	2day	4day	7day	10day	
1yr	0.37	0.58	0.70	0.95	1.16	1.39	1yr	1.01	1.36	1.61	2.11	2.49	3.03	3.49	1yr	2.68	3.36	3.86	4.61	5.22	1yr
2yr	0.42	0.65	0.79	1.08	1.33	1.60	2yr	1.14	1.56	1.82	2.36	2.90	3.55	4.00	2yr	3.14	3.84	4.46	5.23	6.03	2yr
5yr	0.52	0.81	1.00	1.37	1.75	2.04	5yr	1.51	2.00	2.36	3.06	3.81	4.60	5.26	5yr	4.07	5.06	5.85	6.83	7.63	5yr
10yr	0.63	0.97	1.20	1.68	2.17	2.49	10yr	1.87	2.43	2.88	3.74	4.67	5.60	6.52	10yr	4.96	6.27	7.24	8.37	9.28	10yr
25yr	0.82	1.24	1.55	2.21	2.91	3.24	25yr	2.51	3.17	3.76	4.95	6.16	7.24	8.64	25yr	6.41	8.31	9.61	10.99	12.01	25yr
50yr	1.00	1.52	1.89	2.72	3.66	3.99	50yr	3.15	3.90	4.60	6.14	7.59	8.81	10.70	50yr	7.79	10.29	11.92	13.49	14.62	50yr
100yr	1.23	1.86	2.33	3.36	4.61	4.90	100yr	3.98	4.79	5.66	7.64	9.37	10.71	13.28	100yr	9.48	12.77	14.84	16.57	17.84	100yr
200yr	1.52	2.28	2.89	4.19	5.84	6.03	200yr	5.04	5.89	6.96	9.55	11.56	13.02	16.47	200yr	11.53	15.84	18.48	20.37	21.79	200yr
500yr	2.04	3.03	3.90	5.67	8.06	7.96	500yr	6.96	7.78	9.15	12.89	15.28	16.84	21.94	500yr	14.91	21.10	24.74	26.75	28.43	500yr



Post-Development Analysis of the 100-Year Storm Events

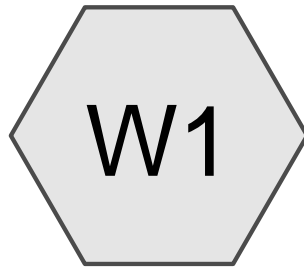

Watershed 1



10 Cultec R-330XLHD



Routing Diagram for Proposed

Prepared by Hudson Engineering & Consulting

HydroCAD® 10.00-20 s/n 02549 © 2017 HydroCAD Software Solutions LLC

Proposed

Type III 24-hr 100-Year Rainfall=8.91"

Prepared by Hudson Engineering & Consulting

HydroCAD® 10.00-20 s/n 02549 © 2017 HydroCAD Software Solutions LLC

Page 2

Summary for Subcatchment W1: Watershed 1

Runoff = 1.39 cfs @ 12.01 hrs, Volume= 4,208 cf, Depth= 8.67"

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 0.00-60.00 hrs, dt= 0.01 hrs
Type III 24-hr 100-Year Rainfall=8.91"

	Area (sf)	CN	Description
*	713	98	Proposed Addition
*	1,091	98	Proposed Garage
*	4,021	98	Proposed Driveway
	5,825	98	Weighted Average
	5,825		100.00% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
1.0					Direct Entry,

Summary for Pond C: 10 Cultec R-330XLHD

Inflow Area = 5,825 sf, 100.00% Impervious, Inflow Depth = 8.67" for 100-Year event
 Inflow = 1.39 cfs @ 12.01 hrs, Volume= 4,208 cf
 Outflow = 0.30 cfs @ 11.67 hrs, Volume= 4,208 cf, Atten= 79%, Lag= 0.0 min
 Discarded = 0.30 cfs @ 11.67 hrs, Volume= 4,208 cf

Routing by Stor-Ind method, Time Span= 0.00-60.00 hrs, dt= 0.01 hrs
 Peak Elev= 3.08' @ 12.37 hrs Surf.Area= 430 sf Storage= 756 cf

Plug-Flow detention time= 10.9 min calculated for 4,208 cf (100% of inflow)
 Center-of-Mass det. time= 10.9 min (746.1 - 735.3)

Volume	Invert	Avail.Storage	Storage Description
#1A	0.00'	294 cf	11.17'W x 38.50'L x 3.54'H Field A 1,523 cf Overall - 544 cf Embedded = 979 cf x 30.0% Voids
#2A	1.00'	544 cf	Cultec R-330XLHD x 10 Inside #1 Effective Size= 47.8"W x 30.0"H => 7.45 sf x 7.00'L = 52.2 cf Overall Size= 52.0"W x 30.5"H x 8.50'L with 1.50' Overlap Row Length Adjustment= +1.50' x 7.45 sf x 2 rows
		838 cf	Total Available Storage

Storage Group A created with Chamber Wizard

Device	Routing	Invert	Outlet Devices
#1	Discarded	0.00'	30.000 in/hr Exfiltration over Surface area

Discarded OutFlow Max=0.30 cfs @ 11.67 hrs HW=0.04' (Free Discharge)↑ **1=Exfiltration** (Exfiltration Controls 0.30 cfs)

Percolation & Deep Hole Test Logs



HUDSON
ENGINEERING
&
CONSULTING, P.C.

SITE ADDRESS: 54 Clinton Avenue

TOWN/VILLAGE: Dobbs Ferry

DATE: 10/29/2021 TIME: 10:52am

WEATHER: Mostly Cloudy TEMP. 50° F

WITNESSED BY: Nicholas Shirriah

DEEP TEST HOLE DATA SHEET – STORMWATER MANAGEMENT SYSTEM

DEPTH	HOLE NO. <u>1</u>	HOLE NO. <u>2</u>	HOLE NO. <u>3</u>	HOLE NO. <u>4</u>
G.L.	0 – 6" Topsoil			
6"				
12"				
18"	6 – 36"			
24"	Fine brown			
30"	Sandy loam			
36"				
42"	36 – 98"			
48"	Mixed sands			
54"	w/ small rocks			
60"				
66"	No Ledge			
72"	No GW			
78"				
84"				
90"				
96"				
102"				
108"				

- Indicate level at which Ground Water (GW), Mottling and/or Ledge Rock is encountered.
- Indicate level for which water level rises after being encountered.

EXCAVATION PERFORMED BY: PRECISION FIELD TESTING



HUDSON
ENGINEERING
&
CONSULTING, P.C.

SITE ADDRESS: 54 Clinton Avenue

TOWN/VILLAGE: Dobbs Ferry

DATE: 10/29/2021 TIME: 11:00am

WEATHER: Cloudy TEMP. 50° F

WITNESSED BY: Nicholas Shirriah

PERCOLATION TEST HOLE DATA SHEET – STORMWATER MANAGEMENT SYSTEM

Owner

HOLE #	CLOCK TIME				PERCOLATION				
Hole Number	Run No.	Start	Stop	Elapse Time (Min.)	Depth to Water From Ground Surface		Water Level in Inches Drop in inches	Soil Rate	
					Start Inches	Stop Inches		Min. per inch	Inches per Hour
# <u>1</u> 4" Ø	1	11:17	11:22	5	22	46	24	0.21	285.71
	2	11:22	11:28	6	22	46	24	0.25	240
	3	11:29	11:38	9	22	46	24	0.375	160
	4	11:39	11:48	9	22	46	24	0.375	160
	5								
# <u>2</u> 4" Ø	1								
	2								
	3								
	4								
	5								
# <u>3</u> 4" Ø	1								
	2								
	3								
	4								
	5								

Notes:

- 1) Tests to be repeated at the same depth until approximately equal soil rates are obtained at each percolation test hole. All data to be submitted for review.
- 2) Depth measurements to be made from top of hole
